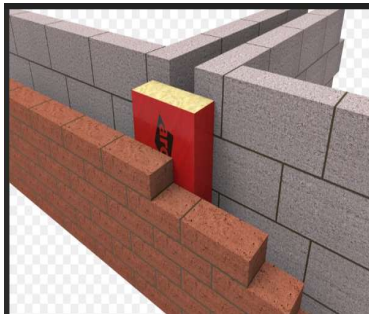


**QUALITY ALERT**

Created By: Ben James (Quality Manager )

Authorised By: James Brown (Director)

|                           |                                                                                              |                                                                                     |          |
|---------------------------|----------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------|----------|
| Business:                 | MIDA Civil Engineering Ltd                                                                   |                                                                                     | ALERT    |
| Title:                    | Firesocks                                                                                    | Reference No:                                                                       | QA49     |
| Issued By:                | Ben James                                                                                    | Issue Date:                                                                         | 27-10-25 |
| Type of Alert:            | Quality & Compliance                                                                         |                                                                                     |          |
| Subject:                  | Firesocks and installation                                                                   |                                                                                     |          |
| Operatives Affected:      | Site Managers                                                                                |                                                                                     |          |
| Details:                  | Ensuring fire socks are put in at brickwork stage and to spec provided by the client         |  |          |
|                           |                                                                                              |                                                                                     |          |
| Action Required:          | Before the plot is handed over to the client any part cavity needs the correct spec firesock |                                                                                     |          |
| Further Information:      |                                                                                              |                                                                                     |          |
| Method for Communication: | Briefing by Site Manager to groundworkers via TBT Alert                                      |                                                                                     |          |
