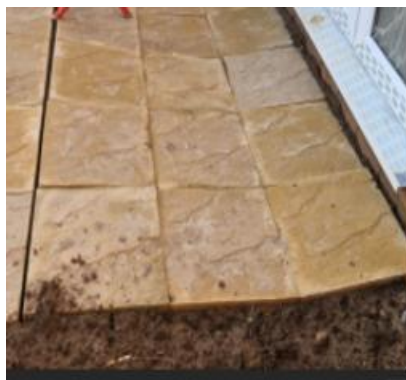


QUALITY ALERT

Created By: Ben James (Quality Manager)

Authorised By: James Brown (Director)

Business:	MIDA Civil Engineering Ltd		ALERT
Title:	Ground Compaction	Reference No:	QA50
Issued By:	Ben James	Issue Date:	27-11-25
Type of Alert:	Quality & Compliance		
Subject:	Ground Compaction and Correct Procedures		
Operatives Affected:	Site Managers		
Details:	Ground Compaction insufficient causing scaffold to fail. Rear slabbing was complete and will now require removal and reinstatement of 5 rears, which has had a knock-on effect to the surrounding fencing.		
Action Required:	Follow correct back fill procedures based on SHW600 which is on the training hub.		
Further Information:			
Method for Communication:	Briefing by Site Manager to groundworkers via TBT Alert		
